Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	7 October 2026
Team ID	
Project Name	Script-Controlled ACL – Restrict Record Access Based on Field Value
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Use the below template to create product backlog and sprint schedule

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Script-Controlled ACL	USN-1	As an administrator, I can create a record-level ACL with a script for the table.	3	High	
Sprint-1		USN-2	As an administrator, I can check the field value (e.g., Sensitivity) inside the ACL script.	3	High	
Sprint-1	Administration & Testing	USN-9	As an administrator, I can create test users and test records with different Sensitivity values.	2	High	
Sprint-1	Field-Value Based Record Restriction	USN-4	As an authorised user, I can open a Confidential record assigned to me.	2	High	
Sprint-1		USN-6	As an unauthorised user, I cannot open or see a Confidential record.	2	High	
Sprint-2	Reusable Access Logic	USN-3	As an administrator, I can move the access logic into a Script Include for reuse.	3	Medium	
Sprint-2	Operation Coverage	USN-5	As an authorised user, I can see the allowed records in the list view and reports.	2	Medium	

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-2		USN-10	As an administrator, I can apply the ACL to the write operation (edit / update).	3	Medium	
Sprint-2	Administration & Testing	USN-7	As a security officer, I can test the ACL by impersonating different users.	3	High	
Sprint-3	Field-Value Based Record Restriction	USN-11	As an administrator, I can make sure an empty or unexpected field value is denied by default.	2	High	
Sprint-3	Administration & Testing	USN-8	As a security officer, I can review the ACL script to confirm the rule for audits.	2	Low	

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	12	6 Days	12 Oct 2026	17 Oct 2026		
Sprint-2	11	6 Days	19 Oct 2026	24 Oct 2026		
Sprint-3	4	6 Days	26 Oct 2026	31 Oct 2026		


Velocity:

The project has 3 sprints of 6 days each, and the total planned work is 12 + 11 + 4 = 27 story points. The planned velocity of the team is 27 / 3 = 9 story points per sprint.

Average velocity (AV) per iteration unit (story points per day) = Sprint Velocity / Sprint Duration = 9 / 6 = 1.5 story points per day.

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. For this project it shows how the 27 planned story points should reduce over the three sprints. The actual line will be added after each sprint ends.

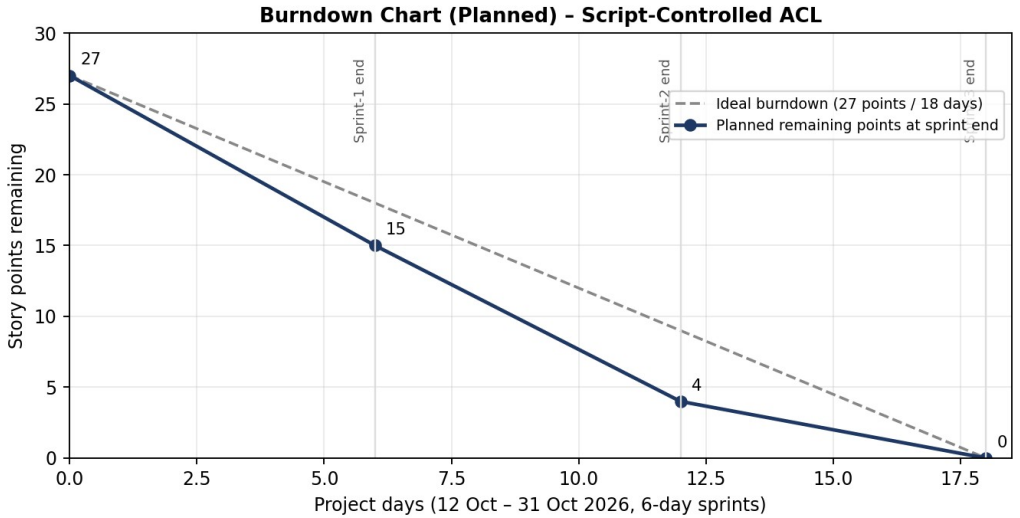

Reference:

https://www.servicenow.com/docs/bundle/zurich-it-business-management/page/product/agile-development/concept/basics-agile-development.html

https://www.servicenow.com/docs/r/4Pll~Vzr5Rr79UNYLnUdJw/uU77liFFv7j4Bx4XUJRRCA

https://docs.servicenow.com/bundle/newyork-it-business-management/page/product/agile-development/concept/agile-development-process-flow.html

https://docs.servicenow.com/bundle/sandiego-it-business-management/page/product/agile-development/task/create-a-story.html

https://www.servicenow.com/docs/r/yokohama/platform-security/access-control/exploring-access-control-list.html?contentId=oczJQGZK~1lGzH~ITrwZHg
